


**Project Evaluation & Review Technique (PERT) and  
Critical Path Method (CPM)**

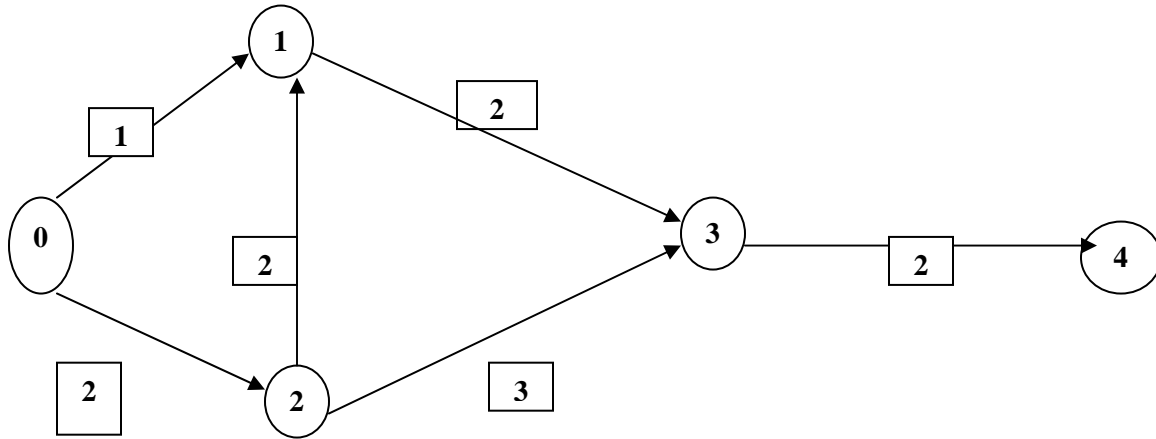

Activity	Time Months	Completion		Float	Dependence	
		Early	Latest			On
0-1	1	1	4	3	I	
0-2	2	2	2	---	I	
2-1	2	4	4	---	D	0-2
2-3	3	5	6	1	D	0-2
1-3	2	6	6	---	D	0-1, 2-1
3-4	2	8	8	---	D	All

<b>CPM</b>	<b>0-2</b>	<b>2-1</b>	<b>1-3</b>	<b>3-4</b>
------------	------------	------------	------------	------------

Path	Path	Time	
1	0-1-3-4	5	
2	0-2-3-4	7	
3	0-2-1-3-4	8	<b>CPM</b>

Activities which can be delayed		
Activity	Months	
0-1	3	
2-3	1	
